



## October 2, 2024 Project Update

### 2024 Street and Utility Improvements

Remember to **SLOW DOWN in Construction Zones** and take extra precautions around construction crews, pedestrians, as well as material & equipment stored within and around the work zones. Follow all posted construction signage and/or detours.

Shabbona Dr – All homes adjacent to the new water main relay should now be connected to the new main. Underground utility work will continue through the end of next week including storm sewer installation. Road grading is anticipated to start the week of October 14<sup>th</sup> with final pavement and restoration completed by the end of November. A reminder that **Shabbona Dr is closed to thru traffic** between Big Foot Country Club and S Lake Shore Dr until Thanksgiving. Access to Big Foot Country Club is from the south only, while access to Country Club Estates beach parking lot and east Abbey Marina parking lot will be from the north off S Lake Shore Dr.

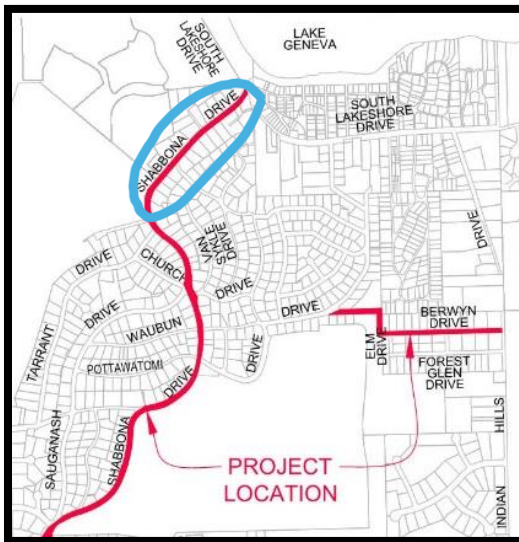

 TrafficSign.com

Feel free to irrigate restored yard restoration areas in front of your property to ensure quick and healthy grass growth.

The anticipated construction schedule may be adjusted because of inclement weather or other factors outside of the Contractor's control. Work by private utilities such as gas, electric, phone and cable are not part of the Village's Contract and may not be reflected in the above schedule. Feel free to contact Village Hall at (262) 275-6136 with any questions.
